



ID	Task Name	Duration	Start	Finish	Calendar
1	<b>St. Johnsbury CSO Oak St. Water, Sewer &amp; Storm Improvements</b>	<b>293 days</b>	<b>Mon 6/18/18</b>	<b>Wed 7/31/19</b>	Jun 8, '18 F T S W
2	Union Street Install 8" Water Main	6 days	Mon 6/18/18	Mon 6/25/18	Jul 1, '18 S T M F T S W
3	Install Road Gravels on Emerson St.	4 days	Tue 6/19/18	Fri 6/22/18	Aug 12, '18 T S W
4	Southard & Russell St. Main Line Sewer	7 days	Tue 6/26/18	Wed 7/4/18	Sep 23, '18 S T M F T S W
5	Install Sewer Services, Southard & Russell	6 days	Thu 7/5/18	Thu 7/12/18	Nov 4, '18 S T M F T S W
6	Southard St. Water Main Install	5 days	Fri 7/13/18	Thu 7/19/18	Dec 16, '18 T S W
7	Water Services, Southard & Russell	5 days	Fri 7/20/18	Thu 7/26/18	Jan 27, '19 S T M F T S W
8	Southard St. Drainage Install CB 20 to CB 27	6 days	Fri 7/27/18	Fri 8/3/18	Mar 10, '19 S T M F T S W
9	Southard St. Drainage Laterals CB 24 & CB 26	2 days	Mon 8/6/18	Tue 8/7/18	Apr 21, '19 F T S W
10	Union St. Remainder of Drainage	4 days	Wed 8/8/18	Mon 8/13/18	Jun 2, '19 F T S W

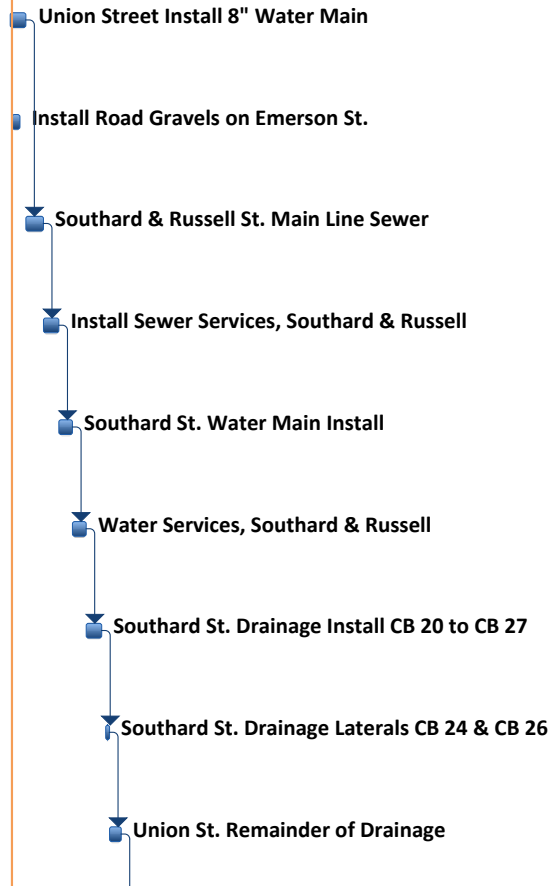

Project: St. Johnsbury CSO Oak St. Draft 4 Date: Tue 6/19/18	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress		

ID	Task Name	Duration	Start	Finish	or 8, '1	May 20,	Jul 1, '18	Aug 12,	Sep 23,	Nov 4, '1	Dec 16,	Jan 27, '1	Mar 10,	Apr 21,	Jun 2, '1
					F	T	S	W	S	T	M	F	T	S	W
11	Install Remaing Sewer Services on Union	4 days	Tue 8/14/18	Fri 8/17/18											
12	Union Street Water Services	6 days	Mon 8/20/18	Mon 8/27/18											
13	Install Road Gravels Union & Southard	5 days	Tue 8/28/18	Mon 9/3/18											
14	Emerson St. Underdrain & Bio-Retension Swale	4 days	Tue 9/4/18	Fri 9/7/18											
15	Southard St. Install Bio-Retention Swale	4 days	Mon 9/10/18	Thu 9/13/18											
16	Union St. Bio-Retention Swale	4 days	Fri 9/14/18	Wed 9/19/18											
17	Paving Emerson St.	2 days	Mon 9/24/18	Tue 9/25/18											
18	Paving Union Street	2 days	Wed 9/26/18	Thu 9/27/18											
19	Paving Emerson Street	2 days	Fri 9/28/18	Mon 10/1/18											
20	Tremont St. Install Drainage 0+00 to 6+75	7 days	Thu 9/20/18	Fri 9/28/18											

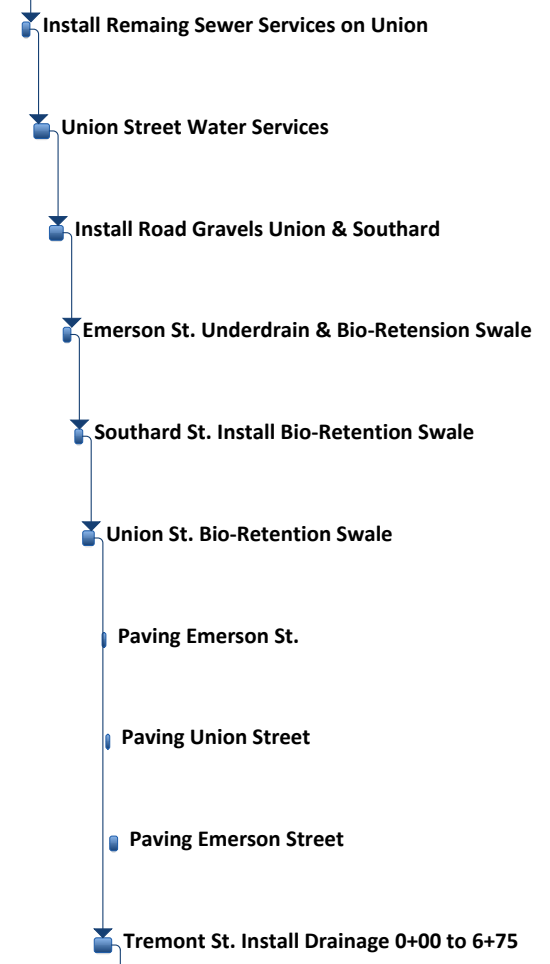

Project: St. Johnsbury CSO Oak St. Draft 4 Date: Tue 6/19/18	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress		

ID	Task Name	Duration	Start	Finish	Calendar
					or 8, '1 F T S W
21	Interconnection Memorial Drive & Tremont St.	1 day	Mon 10/1/18	Mon 10/1/18	
22	Tremont St. Install 8" Water Main 1+00 to 6+25 add Valve Uphill of Hydrant	5 days	Tue 10/2/18	Mon 10/8/18	
23	Tremont St. Install Water Services / Hydrants	6 days	Tue 10/9/18	Tue 10/16/18	
24	Tremont Temp Water from Hydrant at 6+25 to #115, #127 and Unknown Curb Stop	1 day	Wed 10/17/18	Wed 10/17/18	
25	Tremont Water Main 6+25 to Intersection of Emerson	5 days	Thu 10/18/18	Wed 10/24/18	
26	Tremont Drainage 6+75 to CB 13	7 days	Thu 10/25/18	Fri 11/2/18	
27	Paving on Tremont	2 days	Mon 11/5/18	Tue 11/6/18	
28	Clean Up & Restoration	10 days	Wed 11/7/18	Tue 11/20/18	
29	Demobilize	5 days	Wed 11/21/18	Tue 11/27/18	

--	--	--	--	--	--	--

Project: St. Johnsbury CSO Oak St. Draft 4  
Date: Tue 6/19/18

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	
